Impact of Prefabrication Technology & Equipment on Profitability In Construction Industry

Er.Pratiksha Nikalje¹, Prof. Sagar S.Ambure²

¹ Dept of Civil Engineering ²Professor, Dept of Civil Engineering ^{1, 2} Padmabhooshan Vasantdada Patil Institute of TechnologyPune-21

Abstract- Prefabricated buildings and structures are mounted from uniform prefabricated three-dimensional units, providing strength, preset thermal properties of structures, dynamic stability, and immutability of geometric dimensions of the prefabricated elements during their manufacture, transportation, and installation in special and difficult conditions. Prefabrication has been widely regarded as a sustainable construction method in terms of its impact on environmental protection. One important aspect of this perspective is the influence of prefabrication on construction waste reduction and the subsequent waste handling activities, including waste sorting, reuse, recycle, and disposal Suggestions for improvement of the industry and study on cost effectiveness of precast concrete construction. In this project replacement of non-structural component the with prefabrication element is proposed. The cost benefit analysis will be studied including prefabrication element in conventional building.

Keywords- Prefabrication Technology ,Profitability, Construction Industry

I. INTRODUCTION

1.1 General

Prefabrication has been widely regarded as a sustainable construction method in terms of its impact on environmental protection. One important aspect of this perspective is the influence of prefabrication on construction waste reduction and the subsequent waste handling activities, including waste sorting, reuse, recycle, and disposal. Never the less, it would appear that existing research with regard to this topic has failed to take into account its innate dynamic character of the process of construction waste minimization; integrating all essential waste handling activities has never been achieved thus far. This report proposes a dynamic model for quantitatively evaluating the possible impacts arising from the application of prefabrication technology on construction waste reduction and the subsequent waste handling activities

1.2 Objectives

- To study construction process of prefabrication systems.
- To compare prefabrication construction with conventional construction in terms of cost, work breakdown structure and feasibility.
- The object of this seminar is to identify new methodologies in the Construction Industry.
- To identify the cost benefit analysis to change parts of RCC building with prefabrication parts for instance doors and windows frame, prefabrication walls, w.c., bath and staircase.

1.3 Scope of the Project

- Project deals about the theoretical apparatus defining a classification of prefabrication in construction.
- It deals about the criteria that influence the decision on the deployment of prefabricated elements to the project.
- It also brings the results of survey focused on the application of prefabricated construction methods.

II. LITERATURE REVIEW

Vaishali Turai The growth of Indian construction is going to become a fast to fulfill (meet) the need of future generation, time effective and achieving advance technique. The paper based on time comparison of precast concrete vs. cast-in-place (i.e. traditional) concrete. How total time of construction by precast concrete system is less than the time by use of cast-in-place concrete. Time of any construction is directly varied with cost of construction. The time required for steel binding, shuttering, concreting then time required for curing will be minimize (7 days). The Precast is manufactured in factory (i.e. in controlled environment) with required quality, easily mix, and cure till achieved good quantity with desired strength. Precast concrete is manufactured in factory and transport to site. The strength of precast concrete is achieved in greater extent by using high technology, controlled system. For precast construction less manpower is

ISSN [ONLINE]: 2395-1052

required, labors are required only to joint precast members. The time of rework due to improper work, faulty construction method, unskilled labor, material quality, onsite environmental problem can be eliminated by using precast members.

T.Subramani1, M. Muhammad Ansar Prefabricated buildings and structures are mounted from uniform prefabricated three-dimensional units, providing strength, preset thermal properties of structures, dynamic stability, and immutability of geometric dimensions of the prefabricated elements during their manufacture, transportation, and installation in special and difficult conditions. Prefabrication has been widely regarded as sustainable construction method in terms of its impact on environmental protection. One important aspect of this perspective is the influence of prefabrication on construction waste reduction and the subsequent waste handling activities, including waste sorting, reuse, recycle, and disposal suggestions for improvement of the industry and study on cost effectiveness of precast concrete construction. The prefabricated building process usually starts with assembling of the steel, concrete and wood, or pure concrete frames.

Radziszewska-Zielina A Poland to compare the economic benefits of traditional construction methods to prefabricated building systems indicated that the latter provided site labor savings of up to 70% while its incurred total construction where savings of close to 50% are achieved through the use of whole prefabrication methods. These examples are pointers to the immense positive benefits of prefabrication, in addition to reduced energy consumption, waste minimization, mitigation of GHG emission and overall negative environmental impacts. An appraisal of building systems, their characteristics and the challenges they pose to the construction industry, especially in urban, fast-paced regions like the UAE, constitutes the background of this study

Lu, W. and Yuan The construction industry around the globe has been increasingly advocated to utilize prefabrication to minimize waste, thereby alleviating associated negative impacts on environment and the society. Previous studies have reported on waste reduction potential from adopting prefabrication in various economies including Hong Kong. A significant shortcoming of these studies, however, is the neglect of the upstream processes of prefabrication including the manufacturing and transportation of components, which causes construction waste as well. To date it is still unclear how this portion of construction waste is generated and quantified. This study provides insights into understanding construction waste reduction through offshore prefabrication from a holistic view.

III. METHODOLOGY




Fig. 1 Methodology

3.1Prefabrication in housing construction

It is very clear that automation brings great value to businesses. It allows them to achieve higher capacities, improved quality and a wider product range, as well as allowing more options to be offered at significantly higher productivity. Companies that run automated prefabrication thus appear to be very satisfied. As to the question of whether the machine technology pays off, we are seeing a consistently positive image. It is important to think through and plan the transition process precisely. Ideally, experts should be involved at an early stage in the process in order to get the best possible result. By taking a step towards automation, businesses are set up for the future.



Fig 2 prefabrication In Housing Construction

3.2 Prefabrication Elements

- Flooring / Roofing system.
- Precast Beams

IJSART - Volume 6 Issue 8 - AUGUST 2020

- Precast Columns
- Precast wall panels
- Precast Slabs

3.3 Method

- Economy in large scale project with high degree of repetition in work construction.
- Special requirement in finishing.
- Consistency in structural quality control.
- Fast speed of construction.
- Constraints in availability of site resources (e.g. Materials & Laborites)
- Overall assessment of some or all of the above factors which points to the superiority of adopting precast construction over convention method.
- Local Jobs are last.

3.4 Problem Statement

- Name of site: Shivsai developers
- Name of builder : Kiran VitthalNagawade
- Location of site : Plot no. 25&26 at nhawaretal. Shirur, dist. Pune
- Area of site : 6000 sq ft
- Cost of project : 1.8 cr
- Name of consultant : Mahesh kadam
- Details of site :
 - i. 2bhk -- 3 flats per floor
 - ii. 1 bhk 2 flats per floor
- Present condition : excavation and prep for centrelinning for foundation
- Total built up area : 4800 per floor slab area (P+4)
- Owner and developer : kiranNagawade
- Architect : SidheshSonawane
- Structural engineer ; Sachin Sharma
- Total flats : 20 flats
 - i. 12 flats : 2bhk
 - ii. 8 flats : 1bhk
- This structure is conventional residential building. These case study having 20 flats and it is having (P+4) structure.



Fig 3 Elevation plan

IV. RESULT

4.1 Work Breakdown Structure Of Conventional Construction

Ĭ		Aned T	1/7/09	Fri 10,90,09 1st Quert	er jand Qu	arter j3ri	IQuarter	Ath Queter	12	. Quarte		2nd (Juarter		jad Q.		
		Mon 10	Stat: /12/09			Ad	d tasks with date	s to the timeline								Finis Fri 8	h 19,11
		0	Task Node 🗸	Task Name	Duration	, Start	+ Finish	Predecessors +	WTF		ct 11, '09 M T W	T F		18,'09 M T W	T F	Oct 25, 10 S S M T	
	1		ч,	4 SHIVSAI G+4	485 days	Mon 10/12/09	Fri 8/19/11				-	_		_	-		
	2		4	Excavation	15 days	Mon 10/12/09	Fri 10/30/09					-			-	-	
	3		٩	Foundation	10 days	Mon 11/2/09	Fri 11/13/09	2									
	4		4	Murum Filling	4 days	Mon 11/16/09	Thu 11/19/09	3									
	5		4	Slab 1	35 days	Fri 11/20/09	Thu 1/7/10	4									
	6		4	Slab 2	35 days	Fri 1/8/10	Thu 2/25/10	5									
	7		-	Slab 3	35 days	Fri 2/26/10	Thu 4/15/10	6									
	8		٩	Slab 4	35 days	Fri 4/16/10	Thu 6/3/10	7									
	9		4	Slab 5	35 days	Fri 6/4/10	Thu 7/22/10	8									
	10		4	Brickwork	60 days	Fri 7/23/10	Thu 10/14/10	9									
	11		٩	Plaster	29 days	Fri 10/15/10	Wed 11/24/10	10									
	12		4	Plumbing	20 days	Thu 11/25/10	Wed 12/22/10	11									
	13		4	Waterproof	15 days	Thu 12/23/10	Wed 1/12/11	12									
8	14		Ξ.	Tile work	35 days	Thu 1/13/11	Wed 3/2/11	13									
	15		4	Electric work	25 days	Thu 3/3/11	Wed 4/6/11	14									
	16		٩	Painting	33 days	Thu 4/7/11	Mon 5/23/11	15									
	17		4	Lift	40 days	Thu 11/25/10	Wed 1/19/11	11									
	18		4	Drainage	15 days	Thu 1/20/11	Wed 2/9/11	17									
	19		4	Compound wall	11 days	Thu 2/10/11	Thu 2/24/11	18									
	20		4	Watertank	15 days	Fri 2/25/11	Thu 3/17/11	19									
	21		4	Plinth finishing	15 days	Fri 3/18/11	Thu 4/7/11	20									
	22		-	Door window	18 days	Fri 4/8/11	Tue 5/3/11	21									
	23		4	Fabrication	58 days	Wed 5/4/11	Fri 7/22/11	22									
	24			Tab, Light	20 days	Mon 7/25/11	Fri 8/19/11	23									

Fig 4 WBS Of Conventional Construction

14/3	0.03	1st Que	lu e 1,26:00 rter j2nd	Quarter j3	rd Quarter	4th Q	uater	1#Q#	iter	2nd Q	arter	3rd Quarter		
	51att 10on 30,12,09			A	dd tasks with	n dates to th	e timeline						Finish Fri 8/19/11	
	Task Name	Fixed Cost +	Fixed Cost Accrual + T	otal Cost 🔹 👻	Baseline 👻	Variance 🔹	Actual 🔹	Sep 109 30 6 13	Oct '09 20 27 4 1		Nov'09 1 8 15 22	Dec '09	Jan'10 20 27 3 10	1
1	+ SHIVSAI G+4	₹0.00	Prorated	₹ 19,599,840.00	₹ 0.00	19,599,840.00	₹0.00		r					-
2	Excavation	₹ 0.00	Prorated	종 0.00	₹0.00	₹0.00	₹0.00		1					
3	Foundation	₹0.00	Prorated	푸 0.00	₹0.00	₹0.00	₹0.00				`			
4	Murum Filling	₹ 0.00	Prorated	₹ 0.00	₹0.00	₹ 0.00	₹ 0.00				- In			
5	Slab 1	₹ 0.00	Prorated	푸 0.00	₹0.00	₹0.00	₹0.00							
6	Slab 2	₹ 0.00	Prorated	₹ 0.00	₹0.00	₹0.00	₹ 0.00							1
7	Slab 3	₹ 0.00	Prorated	종 0.00	₹0.00	₹0.00	₹0.00							
8	Slab 4	₹ 0.00	Prorated	₹ 0.00	₹0.00	₹0.00	₹0.00							
9	Slab 5	₹ 0.00	Prorated	₹ 0.00	₹0.00	₹0.00	₹ 0.00							
10	Brickwork	₹ 0.00	Prorated	종 0.00	₹0.00	₹0.00	₹0.00							
11	Plaster	₹ 0.00	Prorated	₹ 0.00	₹0.00	₹ 0.00	₹ 0.00							
12	Plumbing	₹ 0.00	Prorated	ই 0.00	₹0.00	₹0.00	₹0.00							
13	Waterproof	₹ 0.00	Prorated	क 0.00	₹0.00	₹0.00	₹ 0.00							
14	Tile work	₹ 0.00	Prorated	ই 0.00	₹0.00	₹0.00	¥ 0.00							
15	Electric work	₹ 0.00	Prorated	₹ 0.00	₹0.00	₹ 0.00	₹ 0.00							
16	Painting	₹ 0.00	Prorated	क 0.00	₹ 0.00	₹0.00	₹ 0.00							
17	uft	₹ 0.00	Prorated	종 0.00	₹0.00	₹0.00	₹ 0.00							
18	Drainage	₹ 0.00	Prorated	₹ 0.00	₹ 0.00	₹ 0.00	₹ 0.00							
19	Compound wall	₹ 0.00	Prorated	ə 0.00	₹0.00	₹0.00	₹0.00							
20	Water tank	₹ 0.00	Prorated	₹ 0.00	₹ 0.00	₹ 0.00	₹ 0.00							
21	Plinth finishing	₹ 0.00	Prorated	₹ 0.00	₹0.00	₹ 0.00	₹ 0.00							
22	Door window	₹ 0.00	Prorated	₹ 0.00	₹0.00	₹ 0.00	₹ 0.00							
23	Fabrication	₹ 0.00	Prorated	₹ 0.00	₹0.00	₹ 0.00	₹ 0.00							
24	Tab, Light	₹0.00	Prorated	주 0.00	₹ 0.00	₹0.00	₹ 0.00							
4							Þ							

Fig 5 Costing Of Conventional Construction

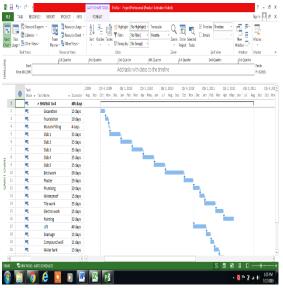


Fig 6 Work Flow Of Conventional Construction

Result from WBS of Conventional Construction from MSP is:

- No. of days 485
- Cost with material+labour-1,96,00,000/-

4.2 Work Breakdown Structure Of Prefabrication Construction

Ger Char		sk gev Task Views	🔜 🖟	e Views *	ZV THE HE Filter	t (No Highlight) * (No Filter) * t (No Group) *	Timescale: [7] Days •	Zoom Entire Selected Project Tasks Zoom	Timeine Timeine Details Split View	New Window	Macros
TMETINE	Sun 9,0	3,09 Start Hot 20,12,09	Fri 11,07,09 1±0,	ate	j ^{2nd Quater} Add tasi	J ^{act Quarter} is with dates to		Quarter	júst Quarter	^{2nd} Quarte	Finish Fri \$13(1)
		0 Task Node	Task Name	Duration	• Start	• Finish	• Predecessors	• Resource Names •	Add New Column	0ct'09 13 20 27 4 11	Nov'09 18 25 1 8
	1	٩.	4 SHIVSAI G+4	415 days	Mon 10/12/09	Fri 5/13/11		Constructon Cost(2		-	
	2	5	Excavation	15 days	Mon 10/12/09	Fri 10/30/09					
	3	5	Foundation	10 days	Mon 11/2/09	Fri 11/13/09	2				
	4	-	Murum Filling	4 days	Mon 11/16/09	Thu 11/19/09	3				1
	5	5	Slab 1	35 days	Fri 11/20/09	Thu 1/7/10	4				
	6	5	Slab 2	35 days	Fri 1/8/10	Thu 2/25/10	5				
	7	4	Slab 3	35 days	Fri 2/26/10	Thu 4/15/10	6				
5	8	5	Slab 4	35 days	Fri 4/16/10	Thu 6/3/10	7				
Š.	9	5	Slab 5	35 days	Fri 6/4/10	Thu 7/22/10	8				
GANTT CHART	10	4	Prefibrication Walls	30 days	Fri 7/23/10	Thu 9/2/10	9				
Ş.	11	4	Plaster	15 days	Fri9/3/10	Thu 9/23/10	10				
0	12	5	Plumbing	20 days	Fri 9/24/10	Thu 10/21/10	11				
	13	4	Waterproof	15 days	Fri 10/22/10	Thu 11/11/10	12				
	14	4	Tife work	35 days	Fri 11/12/10	Thu 12/30/10	13				
	15	5	Electric work	25 days	Fri 12/31/10	Thu 2/3/11	14				
	16	-	Painting	33 days	Fri 2/4/11	Tue 3/22/11	15				
	17	-	Lift	40 days	Fri 9/24/10	Thu 11/18/10	11				
	18	5	Drainage	15 days	Fri 11/19/10	Thu 12/9/10	17				
	19	-	Compound wall	11 days	Fri 12/10/10	Fri 12/24/10	18				
	20	4	Water tank	15 days	Mon 12/27/10	Fri 1/14/11	19				
1									F		
REAL		SINEW TASIS:							8		

Fig 7 WBS Of Prefabrication Construction

Ger That	: 1	ak Glender - Tex age - Collender - Tex Tex Views	Mesource Sheet	AU E Sot Outine	Here 1	(No Filter)	Timescale: [7] Days	Zoom Entire - Project	Q	Indire Timéne	Nev Window	Macros
	Sun 9	13,09 Sunt 11/15 Start Une 03/12/09		jand Qa	atr	^{3rd Quarter} s with dates t	to the timeli	4th Quarter		1st Quarter	2nd Quar	
1	1	Taik Name	Fixed Cost + Fixed	i Cost Accrual + 1 Prorated	Total Cost → 1	taseline + Vari 중 0.00 중 19			wining +	Add New Column	13 20 27	4 11 18 25 1
1	2	Excavation	¥ 0.00	Prorated	₹0.00	₹0.00	₹1.00	₹0.00	₹0.00			
	3	Foundation	₹0.00	Prorated	₹0.00	₹0.00	₹0.00	₹0.00	₹0.00			1
	4	Murum Filling	₹0.00	Prorated	₹0.00	₹0.00	₹0.00	₹0.00	₹0.00			
	5	Slab 1	₹0.00	Prorated	₹0.00	₹0.00	夜0.00	₹0.00	₹0.00			
	6	Slab 2	₹0.00	Prorated	₹0.00	₹0.00	₹0.00	₹0.00	₹0.00			
	7	Slab 3	₹0.00	Prorated	₹0.00	₹0.00	₹ 0.00	₹0.00	₹0.00			
	8	Slab 4	₹0.00	Prorated	₹0.00	₹0.00	₹0.00	₹0.00	₹0.00			
	9	Slab 5	₹0.00	Prorated	₹0.00	₹0.00	₹0.00	₹0.00	₹0.00			
	10	Prefibrication Walls	₹0.00	Prorated	₹0.00	₹0.00	夜0.00	₹0.00	₹0.00			
	11	Plaster	₹0.00	Prorated	₹0.00	₹0.00	₹0.00	₹0.00	₹0.00			
6	12	Plumbing	₹0.00	Prorated	₹0.00	₹0.00	₹0.00	₹0.00	₹0.00			
	13	Waterproof	₹0.00	Prorated	₹0.00	₹0.00	₹0.00	₹0.00	₹0.00			
	14	Tile work	₹0.00	Prorated	₹0.00	₹0.00	₹0.00	₹0.00	₹0.00			
	15	Electric work	₹0.00	Prorated	₹0.00	₹0.00	£ 0.00	₹0.00	₹0.00			
	16	Painting	₹0.00	Prorated	₹0.00	₹0.00	₹0.00	₹0.00	₹0.00			
	17	Uft	至 0.00	Prorated	₹0.00	₹0.00	₹0.00	₹0.00	₹0.00			
	18	Drainage	₹0.00	Prorated	₹0.00	₹0.00	£0.00	₹0.00	₹0.00		om - Im	\$
	19	Compound wall	₹0.00	Prorated	₹0.00	₹0.00	₹0.00	₹0.00	₹0.00	NDA 2020 Exam D		
Î	20 (Watertank	₹0.00	Prorated	₹0.00	₹0.00	₹0.00	₹0.00	₹0.00	Released. Check h		۲
540		NEW TASIS: AUTO SCHEDULED								NI	881	
50	N	HEW TASIS : AUTO SCHEDULED		ρā						NE		

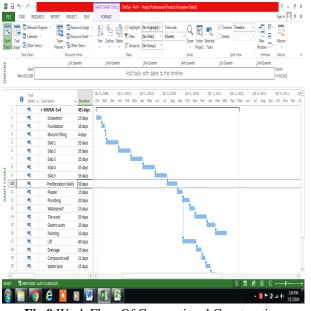


Fig 9 Work Flow Of Conventional Construction

Result from WBS of Prefabrication Construction from MSP is:

- No. of days 415
- Cost with material+labour-1,90,80,000/-

4.3 Comparison Of Conventional Construction To Prefabrication Construction

Туре	Duration	Cost
Conventional Construction	485	19600000
Prefabrication Construction	415	19080000




Fig 10Comparison of Duration for Conventional Construction To Prefabrication Construction




Fig 11Comparison of Cost for Conventional Construction To Prefabrication Construction

V. CONCLUSION

- A comparative survey from site found that prefabrication reduced activities associated with repetitive body movements, ergonomic challenges and ergonomic problems.
- A conventional RCC case study is selected and its cost estimate, schedule and work break down structure in MSP is prepared.
- Prefabrication technology has not transferred as easily when compared with other technologies because it is a production technology or knowledge based and not a consumption technology or product based.
- The survey found that 92% workers reported that the use of prefabrication Preassembly and precast would reduce hazards related to material handling on site and that the reduction of scaffolding through the use of prefabricated preassembly or precast components would lead to less falls on sites.

REFERENCES

- [1] Abhishek K.Taware1' Prefabrication, Sustainable Technique in Building Construction' Volume 1, Issue 2, February 2017
- [2] Aki Aapaoja "the Challenges Of Standardization Of Products And Processes In Construction" Proceedings IGLC-22, June 2014
- [3] EvanjalineLibie "Impact Of Prefabrication On Profitability Over Traditional Construction" ISSN: 2455-5797 Vol. (2), No. (3): June 2016
- [4] Elzbieta Radziszewska -Zielina, Monika Glen. "Studies of the Prefabricated Housing Construction Market in Poland" Journal Of Civil Engineering Vol. 9, Issue 2, 2014

- [5] Gerhard Girmscheid, "Industrialization in Building Construction – Production Technology or Management Concept" Vol. 8, Issue 1, 2012
- [6] H. W. Lee "Macroeconomic Labor Productivity and Its Impact on Firm's Profitability" Journal of the Operational Research Society August 2013
- [7] Hamza Khan "Study on the Trends & Usage of Prefabrication and Modularization: Increasing Productivity in the Construction Industry" ISSN 2278-3652 Volume 8, Number 2 (2017)
- [8] Hong Xue "Factors Affecting the Capital Cost of Prefabrication—A Case Study of China" Published: 24 August 2017.
